


ID	Task Name	Duration	Start	Finish	Jul 12, '09	Jul 19, '09	Jul 26, '09	Aug 02, '0
1	Project Start	0 days	Mon 07/13/09	Mon 07/13/09	S	M	T	W
2	Bore Conduit	8 days	Mon 07/13/09	Wed 07/22/09	T	F	S	S
3	Install Caissons - Complete	5 days	Thu 07/23/09	Wed 07/29/09	S	S	M	T
4	Install conduit Serv & Cont	3 days	Thu 07/30/09	Mon 08/03/09	F	S	S	M
5	Excavate form, pour serv & cont	3 days	Tue 08/04/09	Thu 08/06/09	T	F	S	S
6	Conduit tie ins	4 days	Fri 08/07/09	Wed 08/12/09	S	S	M	T
7	Sawcut for removals	1 day?	Thu 08/13/09	Thu 08/13/09	F	S	S	M
8	Remove curb, gutter, sidewalk	4 days	Fri 08/14/09	Wed 08/19/09	S	S	M	T
9	Form & Pour Curb and gutter	4 days	Thu 08/20/09	Tue 08/25/09	F	S	S	M
10	Grade sidewalk	2 days	Wed 08/26/09	Thu 08/27/09	S	S	M	T
11	Pour sidewalk and ramps	2 days	Fri 08/28/09	Mon 08/31/09	F	S	S	M
12	Install Signs	4 days	Tue 09/01/09	Fri 09/04/09	S	S	M	T
13	Install Poles & Cabinets	4 days	Mon 09/07/09	Thu 09/10/09	F	S	S	M
14	Wire	3 days	Fri 09/11/09	Tue 09/15/09	S	S	M	T
15	Stripe	1 day?	Wed 09/16/09	Wed 09/16/09	F	S	S	M
16	Turn On	1 day?	Thu 09/17/09	Thu 09/17/09	S	S	M	T
17	Clean up	3 days	Fri 09/18/09	Tue 09/22/09	F	S	S	M
18	Project Complete 73 Calendar Days	0 days	Tue 09/22/09	Tue 09/22/09	T	F	S	S

Project: Initial Schedule 6309
Date: Mon 06/29/09



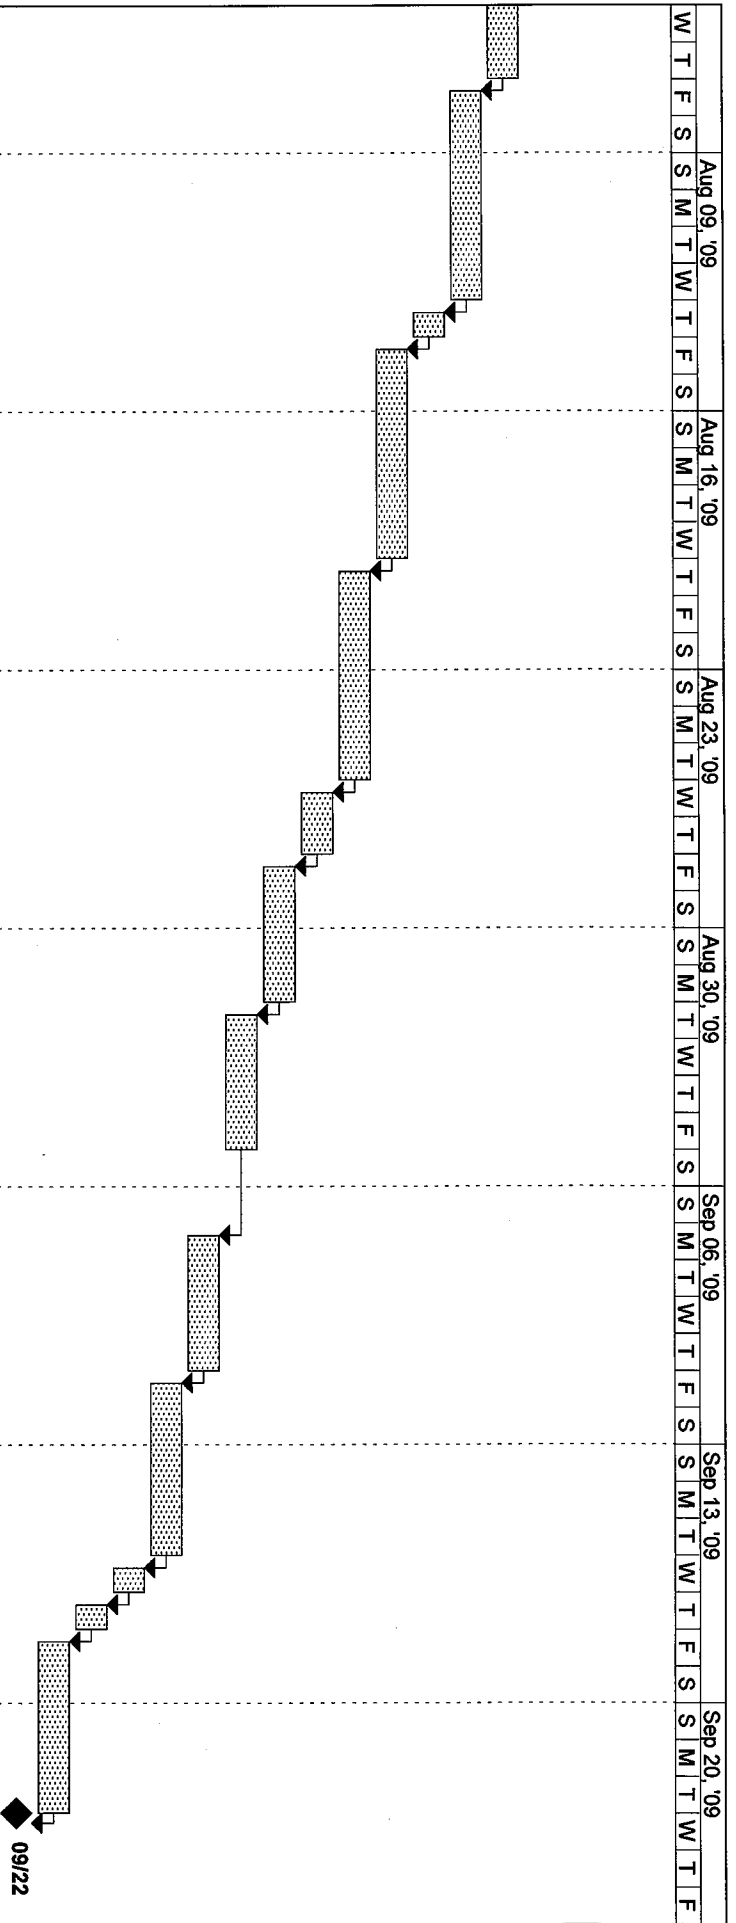

Project: Initial Schedule 6309
 Date: Mon 06/29/09

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	
